

COORDINATION MEETING NOTES PUBLIC WORKS DEPARTMENT

August 8, 2017

Projects Under Construction

1. 2017 Street Resurfacing Contract – Craig Midgett (CEI - SEPI)
 - a. Rose Brothers Paving
 - b. 1st Street – Summit to Jarvis
 - c. Kingsbrook, Dalebrook, Deerwood

Projects Recently Advertised

1. None

Projects in Design/Upcoming Projects

1. South Tar River Greenway Phase 3 – First Street Place to Moye Blvd – Lynn Raynor
 - a. Received approval from CSXT
 - b. Awaiting final draft contract approval from NCDOT
 - c. Tentative Construction advertisement September
2. Safe Routes to School-Craig Midgett
 - a. Currently finalizing easement acquisition
 - b. Construction depends upon completion of acquisition
3. W. 5th Street Gateway – Lynn Raynor
 - a. Currently working on easement acquisition
 - b. Construction depends upon completion of acquisition
4. 2018 Street Resurfacing Contract
 - a. Developing initial streets list
 - b. Tentative advertisement October/November
5. Arlington Bond Project Phase 3
 - a. Hooker to Red Banks, Timeframe unknown

GREENVILLE UTILITIES COMMISSION

~ Electric Department Work Progress ~

August 2017

INSTALLING UG PRIMARY & TRANSFORMERS	
<i>Tenth Street Connector</i> <i>South Bypass Loop</i> <i>GTAC</i> <i>Discount Tire</i> <i>ECU Transit Depo</i> <i>Nicholas Acres Subdivision</i> <i>1245 Sugg Parkway (Shell Bldg.)</i>	<i>Lynndale East (Sec. 4; Ph. 2)</i> <i>Langston Farms (Sec. 8 & 9)</i> <i>Sagewood Subdivision (Ivy Rd)</i> <i>The Gathers (old Pugh's lot)</i> <i>Brook Hollow (Sec.; Ph. 2)</i> <i>Alton Village</i> <i>Brandy Creek</i> <i>College View Apartments</i> <i>Sidewalk Group Apartments</i> <i>Poplar Grove Subdivision (Sec. 3)</i>
** RED ITEMS ARE BEGINNING SOON **	

<u>NAME</u>	<u>WORK TO BE DONE</u>	<u>DURATION</u>
Dickinson Ave (DOT Project)	Maintenance & Relocation of Facilities	Continues
Villa Grande S/D	Add Primary, TX & Lights	Continues
CHE- Mid-Atlantic Inc.	Install Secondary	Continues
1000 Staton Rd (Sunbelt)	Install Tx & Secondary	Continues
Tuesday's	Install new UG & Secondary	Continues
Panera Bread	Install new UG Primary & TX	Continues
Langston Farms (Sec 8 & 9)	Install Lights	Continues
Taft/Ward - Tenth St Apts.	Remove OH Primary	Beginning Soon
Robert Little Rd (DOT Project)	Drain Tile Replacement	Beginning Soon
NC 33E (DOT Project)	Replacing old UG cable	Beginning Soon
Physicians East	Add Primary & TX for Addition	Beginning Soon

8/8/2017

GREENVILLE UTILITIES COMMISSION
Water Resources Department Work Progress

August 2017

WATER RESOURCES DEPT. PROJECTS

<u>Name</u>	<u>Work to be Done</u>	<u>Duration</u>
River Bluff Drive	Install inline valves	1 day
10 th St. Connector	Valve/drop installs	1 week
GTAC	Replace sewer on Pitt & Clark	6 weeks
Town Creek Culvert	Install valves & thrust blocking	6 weeks?
Rehab sewer mains & services	About town	1 month

DEVELOPER PROJECTS

Projects Approved for Construction

Audi of Greenville (UC)
Blackwood Ridge Phase 1
Centre Court (UC)
College View Apartments (UC)
Discount Tire (UC)
ECU-Clement Hall (UC)
ECU-Student Union (UC)
ECU-Faculty Way (UC)
Elmhurst Elementary (UC)
Fairfield Inn (UC)
GTAC (UC)
Lynndale East Section 4, Phase 2 (UC)
Meadow Woods (UC)
Mill Creek (UC)
Oxford Park (UC)
Ronald McDonald House (UC)
Sagewood (UC)
Savannah Place Sec. 2 Ph. 1&2 (UC)
Savannah Place Sec. 4 Ph. 1&2 (UC)
The Gather Uptown Apartments (UC)
The Salvation Army
University Edge (UC)
Vidant Cancer Center
Westhaven South Section 2 (UC)
Wirth Chiropractic (UC)

Projects Completed & Accepted by GUC

Parkside Bluffs
South Pitt Street
Brook Hollow Sec. 4 Phase 2
Publix
Taft Ward Sewer
Figure Eight
Arbor Hills Phase 5
Theta Chi Fraternity House
Children's World
Langston West 8 & 9
Dollar General (Frog Level)

GREENVILLE UTILITIES COMMISSION

Gas Department Work Progress

August 2017

<u>NAME</u>	<u>WORK TO BE DONE</u>	<u>DURATION</u>
Ms. Paul Lane	Abandon 2" WS main and install 2" PE main.	5 Days
Langston West Section 7	Install 2" PE Gas Main	5 Days
Paramore SD – Becky Anne Dr	Install 506' X 2" PE Gas Main	2 Days
J C Galloway Road	Install 200' X 4" PE Gas Main	3 Days
Greenville Housing Authority	Remove Master Meters	6 Days
Autumn Lakes – Robert Little Rd	Install 742' X 4" PE and 3,142' X 2" PE Gas Main	5 Days
Savannah Place	Install 2" PE Gas Main	4 Days
Summer Winds (Winterville)	Install 2" PE Gas Main	6 Days
Boyd Street – Winterville	Relocate 2,300' X 4" PE Gas Main	20 Days

CONTRACTOR PROJECTS

Thomas Langston Road (Improvements)	Install 8" PE Gas Main	15 Days
Southwest Bypass	Relocate existing facilities	40 Days

ON HOLD PROJECTS

E Wright Rd. – (Greenville) Phase 2	OB Replacement Project	10 Days
Colonial Heights – (Greenville) Phase 3	OB Replacement Project	20 Days
6" Service Tap Replacement Project	Replace Leaking Taps	365 Days
About System	Replace White Bottom Valves	Until Complete

SUDDENLINK	
8/8/2017	
NBR	Type work
Dunhagen	New Build Residential
Ayden Golf Club Road	New Build Residential
Black Jack North G224A	New Build Residential
Black Jack North G231A	New Build Residential
Black Jack South G233A	New Build Residential
Twin Lakes Campgrounds	New Build Residential
Glen Castle @ Irish Creek	New Build Residential
Cobblestone	New Build Residential
Arbors	New Build Residential
Brandy Creek Ph2	New Build Residential
Brookfield Ext	New Build Residential
Greenbriar Place	New Build Residential
33 East Apartments	New Build Residential
Cambria Dr Phase 4	New Build Residential
Beddard Heights	New Build Residential
IM	Type work
Reedy Branch Rd	Forced relocate
South West By Pass	Forced relocate
Old Snow Hill Road Ph1	Forced relocate
Davenport Farm Road Ph2	Forced relocate
US 13 Phase 3	Forced relocate
NC 102 W Phase 4	Forced relocate
Wildwood Dr Phase 5	Forced relocate
Pocosin Road Phase 6	Forced relocate
11th St Apartments Phase 2	Forced relocate
ECU Clement Hall	rebuild
Mills Rd G179	Forced relocate
Barrus Construction Rd	Forced relocate
Kristin Dr	rework PS
407 W 4st St	meter PS
Baywood Power supply	Permit PS
Kings Rd	WQ PS
University Suites	Raise PS to GL
Honolulu Cell Site	AFO design
US 17 ring	AFO design
G088 Old River Rd	AFO design
Myrtle Ave	Forced relocate
3030 Greenville Blvd	PCO's
1803 W 3rd St	Cable replacement
Northwest MHP	Cable replacement
2919 Major Smith Rd	Status monitoring
3606 Masters Lane	Cable replacement
705 McDonald St	Cable replacement
700 Compton	Cable replacement
3858 Frog Level Rd	Cable replacement
4318 Charles Blvd	Cable replacement
1687 Rams Horn Road	Cable replacement
5419 Reedy Branch Road	Cable replacement
Cyprus Glen 208 Hickory Dr	Cable replacement
Bayswater Drive G053A	Cable replacement
Corey at Van Gert	Cable replacement

Date: 8/8/2017

County:

22

Date:

2017

[illegible]



Pitt County



August 2017

Statewide Ticket and Transmission Data

July: 2017 / 2016 Comparison

Tickets

2017: 160,565

2016: 166,259

Difference: -3.4%

Transmissions

2017: 909,697

2016: 909,182

Difference: 0.1%



Statewide Ticket and Transmission Data

Year-to-Date: 2017 / 2016 Comparison

Tickets

2017: 1,129,684

2016: 1,099,987

Difference: 2.7%

Transmissions

2017: 6,409,492

2016: 5,902,076

Difference: 8.6%



County Ticket Volume



July: 2017 Stats Compared with 2016

	Type Ticket					
	3 HR	CNCL	NEW	RXMT	UPDT	TOTAL
2016	10	14	1106	13	459	1602
2017	7	24	1179	48	706	1964
+/- Var	-30.0%	71.4%	6.6%	269.2%	53.8%	22.6%
				Locates per day		98

County Ticket Volume



Year-to-Date: 2017 Stats Compared with 2016


	Type Ticket					
	3 HR	CNCL	NEW	RXMT	UPDT	TOTAL
2016	54	119	7816	72	2522	10583
2017	54	138	7877	169	4199	12437
+/- Var	0.0%	16.0%	0.8%	134.7%	66.5%	17.5%
				Locates per day		85

County Ticket Distribution



County/Place	07 Jul
PITT	1964
AYDEN	95
BALLARDS CROSSROAD	1
BELL ARTHUR	14
BELVOIR	15
BETHEL	11
CHICOD	8
FALKLAND	10
FARMVILLE	124
FOUNTAIN	8
GREENVILLE	1375
GRIFTON	20
GRIMESLAND	62
PACTOLUS	3
SHELMERDINE	2
SIMPSON	8
WINTERVILLE	208

A Safety Moment

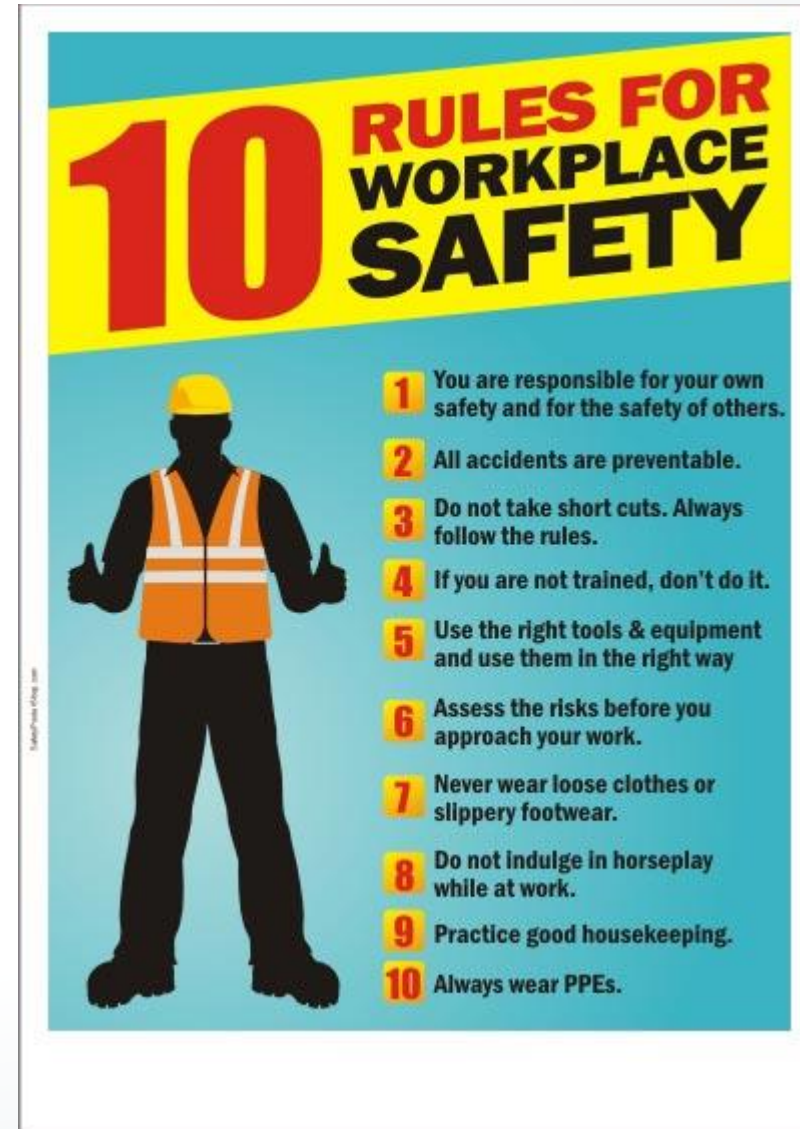

Events, Meetings, Holidays



Upcoming Holiday

Labor Day
Monday, Sept. 4

*All holidays are excluded from
the three working day notice.*

Board Meeting

3Q17
October 19-20
Double Tree by Hilton Hotel
New Bern River Front
New Bern, NC

NC Underground Damage Prevention Review Board Meetings

**Located at: 2550 Operations
Way, Raleigh, NC.**

On the corner of Operations
Way and Westinghouse Blvd.

October 17, 2017
10am to 4pm

State UCC Meetings

PSNC Energy

Tue, Sept. 12, 2017

10am – 12pm

1801 Trinity Church Rd.,
Concord, NC 28027

August 11, 2017



Join us at the ballpark



Asheville Tourists
Fri, August 11th
30 Buchanan Pl,
Asheville, NC

Our co-sponsor of this game is:



Join us at the ballpark



Durham Bulls
Fri, August 11th
409 Blackwell St,
Durham, NC

Our co-sponsor of this game is:



Join us at the ballpark



Charlotte Knights
Thurs, Aug. 17th
324 S Mint St,
Charlotte, NC

Our co-sponsor of this game is:



Have you registered yet?



MOCK LINE STRIKE
EDUCATION THROUGH DEMONSTRATION

ncpipesplus.org/mock-line-strike.html

September 13th 2017

NC State Fairgrounds &
Kerr Scott Building
1025 Blue Ridge Rd,
Raleigh, NC 27607



North Carolina 811
www.nc811.org

How can an 811 liaison help you today?



Get a PDF copy of this presentation at www.ncucc.org

Use the UCC Issues form to voice your concerns to both local and state level UCC meetings in North Carolina. Available on both the NCUCC website and the NC811 app.

Like and follow us on:



facebook.com/nc811
twitter.com/NC_811
