

County: 7th Date: 5/8/2018

Date: 5/8/2018

[illegible]

GREENVILLE UTILITIES COMMISSION

~ Electric Department Work Progress ~

May 2018

INSTALLING NEW UG PRIMARY & TX	BEGINNING SOON
<i>Tenth Street Connector Koinonia Christian Center Charleston Village (Phase 2) Taberna (Phase 4) Mill Creek (Phase 2) 20/20 Vision Center College View Apartments Lynndale East (Sec. 4; Ph. 2) Savannah Place (Sec 4; Ph. 1& 2) Summer Place (NC 33E) Meadow Woods (Phase 2) The Drake Apartments</i>	<i>Salvation Army ECU Transit Depo ECU Student Union Langston Farms (Phase 3) Emerald Park (Phase 2) ECU Telecom Allen Rd (DOT Pole Relocation Project) NC 11 & 43 N (DOT Pole Relocation Project) Dickinson Ave (DOT Maintenance Project) Boyd Rd (DOT Drain Tile Replacement Project) The Legacy @ Firetower Junction Pitt County Animal Shelter Laurel Oaks Subdivision Cheshire Subdivision</i>

<u>NAME</u>	<u>WORK TO BE DONE</u>	<u>DURATION</u>
Ignite Church	Add Primary & TX	<i>In Progress</i>
Kenilworth Subdivision	Install new UG Cable & TX	<i>In Progress</i>
Langston Farms (Sec 8 & 9)	Install Lights	<i>In Progress</i>
Greenville Carwash	Install new UG Cable & TX	<i>In Progress</i>
Brook Hollow (Sec 4; Ph. 3)	Add Primary & TX	<i>Beginning Soon</i>
Eastern Dermatology	Relocating TX	<i>Beginning Soon</i>
Proximity Apartments	Install new UG Cable & TX	<i>Beginning Soon</i>
Arbor Hills (new section)	Install new UG Cable & TX	<i>Beginning Soon</i>
Bancroft Ave	Replacing primary poles & post light installations	<i>Beginning Soon</i>
Allen Rd (DOT Project)	Relocating Poles	<i>Beginning Soon</i>
NC 11 & 43 N (DOT Project)	Relocating Poles	<i>Beginning Soon</i>
University Edge	Set TX & Lighting Circuit	<i>Beginning Soon</i>
South Pitt St	Removing OH; Setting UG TX's	<i>Beginning Soon</i>
Atlantic Ave Parking Lot	Install Lighting	<i>Beginning Soon</i>
Hwy 30 (Chicken Houses)	Pull primary; set 2 TX's	<i>Beginning Soon</i>
Airport Hanger	Bore Secondary	<i>Beginning Soon</i>

GREENVILLE UTILITIES COMMISSION

Water Resources Department Work Progress

May 2018

WATER RESOURCES DEPT. PROJECTS

<u>Name</u>	<u>Work to be Done</u>	<u>Duration</u>
River Bluff Drive	Install inline valves	1 day
10 th St. Connector	Valve/drop installs	1 week
GTAC	Replace sewer on Pitt & Clark	3 weeks
Town Creek Culvert	Install valves & thrust blocking	6 weeks ?
Rehab sewer mains & services	about town	1 month

DEVELOPER PROJECTS

Projects Approved for Construction

Arbor Hills 6 (UC)
Berkley Phase 3
Brook Hollow Section 4, Phase 3 (UC)
Charleston Village Sec. 7 (UC)
College View Apartments (UC)
Dowdy Ficklen Southside Renovation (UC)
Drake (UC)
ECU-Student Union (UC)
FEDEX (UC)
GTAC (UC)
Ignite Church (UC)
Legacy (UC)
Meadow Woods (UC)
Mill Creek (UC)
Oxford Park (UC)
Proximity (UC)
Savannah Place Sec. 4 Ph. 1&2 (UC)
Taberna Phase 4(UC)
The Salvation Army
University Edge (UC)
Westpointe Village Section 11 (UC)
Westhaven South Section 2 (UC)

Projects Completed & Accepted by GUC

Carmax
Blackwood Ridge Ph. 1
Sagewood
Savannah Place Sec 2, Phase 1
The Gather Uptown
Lynndale East Section 4, Phase 2

GREENVILLE UTILITIES COMMISSION

Gas Department Work Progress

May 2018

<u>NAME</u>	<u>WORK TO BE DONE</u>	<u>DURATION</u>
Fourth Street and Evans (Alley) - Greenville	Abandon 2" PE Main	1 Day
Verbena Way – Winterville	Install 2" PE Gas Main	1 Day
Westgate Drive	Install 2" PE Gas Main	
Dowdy-Ficklen Stadium	Abandon and Install 4" PE Gas Main	5 Days
Alton Village	Install 2" PE Gas Main	5 days
Summer Winds - Winterville	Install 2" PE Gas Main	6 Days
Savannah Place Phase 2	Install 2" PE Gas Main	4 Days
Greenville Housing Authority	Remove Master Meters	6 Days
Dickinson Ave – Memorial Dr to Reade Circle - Greenville	Relocate conflicts	Until
Cypress Glenn – Greenville	Relocate and Install 2" PE Gas Main	5 Days
US 13(Memorial Dr.) and NC 43 (5 th Street) – Greenville	Relocate Gas Main DOT Project	7 Days

CONTRACTOR PROJECTS

Thomas Langston Road (Improvements)	Install 8" PE Gas Main	30 Days
-------------------------------------	------------------------	---------

ON HOLD PROJECTS

E Wright Rd. – (Greenville) Phase 2	OB Replacement Project	10 Days
Colonial Heights – (Greenville) Phase 3	OB Replacement Project	20 Days
6" Service Tap Replacement Project	Replace Leaking Taps	365 Days
About System	Replace White Bottom Valves	Until Complete

COORDINATION MEETING NOTES PUBLIC WORKS DEPARTMENT

May 8, 2018

Projects Under Construction

1. Atlantic Ave. Parking Lot A – Lynn Raynor
 - a. Power/phone to be relocated along Bonner's Lane
 - b. Waterline to be relocated along Atlantic Ave.
 - c. Placing stone on lot
2. 17-18 Stormwater On-Call – Kevin Leigh
 - a. Trader Construction
 - b. Completing Glasgow; next York, Hooker

Projects Recently Advertised

3. 2018 Street Resurfacing Contract – Lynn Raynor/Gentry Coward
 - a. Re-advertised – Bid opening May 10th
 - b. June Council award
 - c. Probable NTP after 7/4

Projects in Design/Upcoming Projects

1. South Tar River Greenway Phase 3 – First Street Place to Memorial Dr. – Lynn Raynor
 - a. Submitted for additional funding to NCDOT
2. Safe Routes to School – Lynn Raynor
 - a. Awaiting approval from Historic Preservation Office
 - b. Construction NTP late Summer
3. W. 5th Street Gateway – Lynn Raynor
 - a. Beginning easement acquisition
 - b. Construction depends upon completion of acquisition (6-8 months)
4. Arlington Bond Project Phase 3 – Lynn Raynor
 - a. East Group selected
 - b. Preparing design contracts

May 2018



Pitt County



Locate Requests & Transmissions

Apr. 2018 vs 2017

Tickets

2018: 175,205

2017: 156,103

Difference: 12.2%

Transmissions

2018: 997,418

2017: 889,980

Difference: 12.1%

Year-to-Date

Tickets

2018: 664,073

2017: 623,623

Difference: 3.3%

Transmissions

2018: 3,613,848

2017: 3,532,442

Difference: 2.3%

County Ticket Volume

2018 Stats
Compared
with 2017

	Type Ticket					
	3 HR	CNCL	NEW	RXMT	UPDT	TOTAL
2017	15	28	1034	15	531	1623
2018	60	30	1532	59	598	2279
+/- Var	300.0%	7.1%	48.2%	293.3%	12.6%	40.4%
				Locates per day		109



County Ticket Volume

YTD stats
compared
with previous
year

	Type Ticket					
	3 HR	CNCL	NEW	RXMT	UPDT	TOTAL
2017	30	83	4216	95	2194	6618
2018	100	66	5130	183	2399	7878
+/- Var	233.3%	-20.5%	21.7%	92.6%	9.3%	19.0%
				Locates per day		94



County Ticket Distribution




County/Place	04 Apr
PITT	2279
AYDEN	108
BELL ARTHUR	1
BELL FORK	25
BELVOIR	5
BETHEL	10
CHICOD	15
FALKLAND	5
FARMVILLE	90
FOUNTAIN	3
GREENVILLE	1427
GRIFTON	213
GRIMESLAND	77
LAKE ELLSWORTH	1
PACTOLUS	9

PAIGE	1
STOKES	19
TUCKER ESTATES	1
WASHINGTON HEIGHTS	2
WINTERVILLE	267

Incidents

811 Notified	Events	% of Grand Total
Y	598	87.17%
N	88	12.83%
Grand Total	686	100.00%

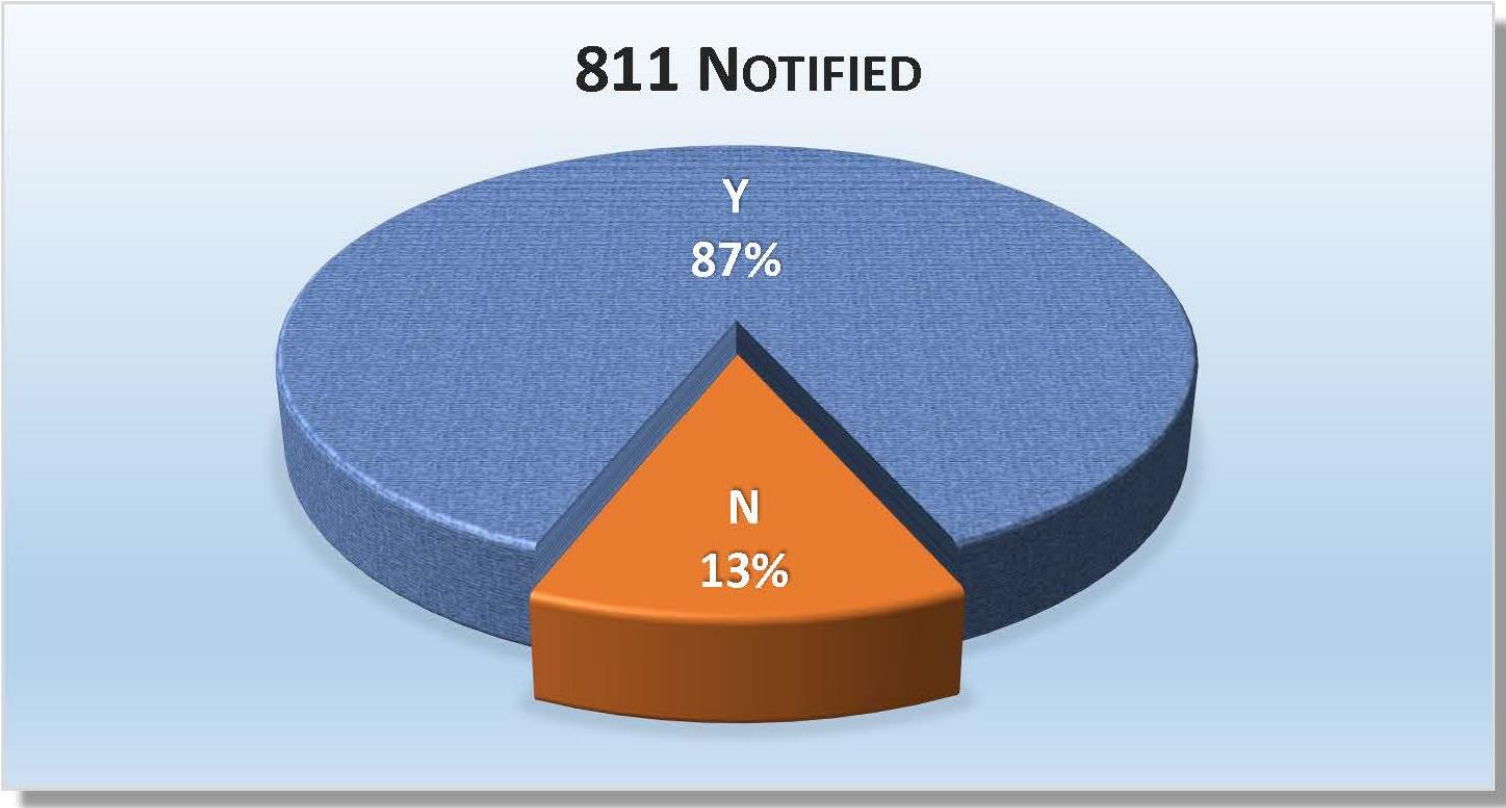

NC811, March 2018: 686 Damage Events in 66 Counties

Incidents

By Events

County	Events	% of Grand Total
Mecklenburg	125	18.22%
Wake	124	18.08%
Guilford	32	4.66%
Johnston	31	4.52%
Durham	30	4.37%
Union	25	3.64%
Cumberland	24	3.50%
Forsyth	22	3.21%
Brunswick	21	3.06%
New Hanover	19	2.77%
Cabarrus	17	2.48%
Gaston	15	2.19%
Davidson	11	1.60%
Harnett	11	1.60%
Lee	10	1.46%
Alamance	9	1.31%
Buncombe	9	1.31%
Orange	9	1.31%
Franklin	8	1.17%
Pitt	8	1.17%
Chatham	7	1.02%
Iredell	7	1.02%
Lincoln	7	1.02%
Moore	7	1.02%
Cleveland	6	0.87%
Craven	6	0.87%
Dare	6	0.87%
Rutherford	5	0.73%
Stanly	5	0.73%
Pender	5	0.73%
Henderson	4	0.58%
Caldwell	3	0.44%
Catawba	3	0.44%



Duplin	3	0.44%
Hoke	3	0.44%
Onslow	3	0.44%
Robeson	3	0.44%
Rowan	3	0.44%
Carteret	2	0.29%
Granville	2	0.29%
Halifax	2	0.29%
Jackson	2	0.29%
Montgomery	2	0.29%
Nash	2	0.29%
Person	2	0.29%
Randolph	2	0.29%
Richmond	2	0.29%
Surry	2	0.29%
Wayne	2	0.29%
Yadkin	2	0.29%
Anson	1	0.15%
Bertie	1	0.15%
Clay	1	0.15%
Davie	1	0.15%
Edgecombe	1	0.15%
Gates	1	0.15%
Haywood	1	0.15%
Macon	1	0.15%
Martin	1	0.15%
Polk	1	0.15%
Rockingham	1	0.15%
Sampson	1	0.15%
Stokes	1	0.15%
Tyrrell	1	0.15%
Vance	1	0.15%
Wilson	1	0.15%
Grand Total	686	100.00%

NC811, March 2018: 686 Damage Events in 66 Counties

BURIED
TELEPHONE
CABLE

WHITE PAINT OR FLAGS ON A JOB SITE ELIMINATES GUESSWORK.

Sometimes it is difficult for excavators to relay the exact location of their dig sites to the one call center. Even clear and accurate information relayed in writing or verbally to one person may not be clear to another. With white lining, locators have excavation information on paper, and also have a clearly marked excavation area. White lining helps to avoid misinterpretation and allows for more accurate locates.

For more info: nc811.org/white-lining.html







PIPES PLUS

**FREE ONLINE
SAFETY TRAINING**

ncpipesplus.org



EVENTS



BOARD MEETING

For booking info reach out to
Tonya Hargraves
tonya@nc811.org

2Q18

July 20, 2018
Lake Lure, NC

3Q18

October 19, 2018
New Bern, NC

For more details visit:
nc811.org/board-info.html

NC Underground Damage Prevention Review Board Meetings

Located at: 2550 Operations Way, Raleigh, NC

- July 17, 2018 - 10am to 4pm
- October 16, 2018 - 10am to 4pm



State NCUCC Meetings



- July 10, 2018
10am to noon in Hickory, NC
at Piedmont Natural Gas
- September 11, 2018
10am to noon in Concord, NC
at PSNC Energy

For more details visit: nc811.org/events.html

NC811 EDUCATION DEPARTMENT



Ann



Howard



Tami



Brian



Kevin



Steve

**Thank you for your time and attention.
You can get a PDF copy of this presentation
on www.ncucc.org**

Use the UCC Issues form to voice your concerns
to both local and state level UCC meetings in North Carolina.
Available on both the NCUCC website and the NC811 app.

