

UCC Sign-In Sheet

County: Pike Date: 7/1/2025

[illegible]

City of Greenville Capital Projects (7/1/2025)

2025 Street Rehabilitation and Preservation (Annual Contract)

- ADA Ramps Complete. Backfill and seeding remain
- Micro surface on Bayswater Drive, Planters Walk Subdivision, and Arbor Hills Subdivision are still underway.
- Concrete work on Bismark. Scheduled to be milled and resurfaced next week.

2024 Stormwater Repairs Contract (Annual Contract)

- Pipe work is finished on Lawrence Street. Curb and asphalt patching scheduled for this week pending weather. Last Task Order for this contract.

2025 Stormwater Repairs Contract (Annual Contract)

- The first 4 task orders are for 9th Street (Washington to crossing Evans), Berkshire, Castlewood, and Remington Drive (at Compton)
- Work is scheduled to begin on 9th Street next week (7/7 NTP)
- **The contractor has expressed concerns over the water mains that will potentially be impacted on Evans/9th Street (110 years old) and Castlewood.**

Cedar Ln Stormwater Improvements

- Postponed until further notice.

Rock Springs Bridge Replacement

- Rocksprings is still in talks w/ Historical society/DEQ and others.

W. 5th Street Reconstruction, Phase 2-4 (BUILD Grant)

- Punchlist items being addressed on D.
- Roundabout to open.
- Evans to open possibly this week.
- Pitt St waterline work starting.

BUILD Grant Greenways

- Project F paved and close to completion.
- Project G extension path installed. Lights and pavilion left.
- Lighting to possibly begin being installed mid-late July per GUC

Greenbrier Culverts and Stream Restoration

- Currently on Hold.

Cedar Stream Restoration

- Postponed for possible federal earmark. Not progressing. No funding is available at the moment.

Arts District Streetscape

- Gateway on hold. Working with NCDOT.
- The sidewalk on Pitt Street is finished.
- Project Deadline December 2026.

St. Andrews Streambank Restoration

- 2nd Public Meeting scheduled for July 8th.
- Currently working on 90% Design and property owner outreach.
- 90% plans are scheduled to be finished by October 2025.

Eppes Community Center Pathway

- The Municipal Agreement is signed by NCDOT.

Drainage Improvements and East Fire Tower Road Project

- Survey and topo being performed by KCI.

Arlington Sidewalk Project

- Working through the contract and schedule with The East Group.
- The Municipal Agreement has been approved.
- Project Deadline September 2026.

Corey Road Regional Detention and Stream Restoration Project

- Design Build with TA Loving
- 60% design completed
- Will need to get construction started shortly to meet funding deadlines.

North-South Connector Project

- Revising TIA based on NCDOT comments
- Engaging property owners and exploring alternative routes to eliminate NCDOT concerns
- Funding deadline of September 1, 2026

GREENVILLE UTILITIES COMMISSION

Electric Department Work Progress

-July 2025 -

ELECTRIC DEPT. PROJECTS

<u>Name</u>	<u>Work to be Done</u>	<u>Duration</u>
Service Installations	About System	ongoing
Rotten Pole and Pole Replacements	Replace Rotten Poles About System	ongoing
Install Area Lights/Main	Installing Area Lights About System	ongoing
LED Light Conversions	About System	ongoing
System Main/Repairs	About System	ongoing
Area Light Cable Replacements	About System	ongoing
Primary Cable Replacements	About System	ongoing
Pole Relocations	About System	ongoing

Lake Glenwood Cable Replacement
Beddard Rd. pole replacement and reconductor
Mobley's Bridge Rd. pole replacement and reconductor

Residential/Commercial DEVELOPER PROJECTS

PCC Welding Center	Carolina Crofts S/D ph1
Tucker Hill Farm S/D ph2	Cypress Glen Expansion
Davenport Farms	Davenport Farms ph9
Cobblestone sec. 3	Williams Farm S/D (Wolf Pit Rd.)
Ample Storage	The Enclave
Azure Vascular Care on Emerald Dr.	Boviet
Evolve at the Pines	Marlboro Spec. Bldg. (Sugg pky)
Wawa (Stantonsburg&10 th St.)	Home 2 Suites (Moye)
Langston Farms ph11	Carter Ridge ph2
Wellingham Commons Flex Bldg.	North State Steel
Kinsaul West S/D	Coastal Plains Shooting Academy
Abbott Trails	Ambrose Bay
COG W. Fifth St. Project	ECU Med. Cup Bldg
Cypress Glen Retirement Expansion	4 th St. Project
Arbor Hills ph12&13	Pair Electronics
Villa Grande ph3	Savannah Place
Apple Park	
Bells Fork Village Apts	
Belmont Apts at Bayswater	
Nipro	

TRANSMISSION PROJECTS

Mt. Pleasant to Sugg Parkway
G230S to Simpson

Light Projects

DOT
Allen Rd



Greenville Utilities Natural Gas Department Project List

Projects InProgress

Notes

1. GUC Annual Leak Survey: Leak Repair
2. Build Grant Project: Contractor working at several locations along 5th Street. The Gas Department is performing gas relocations as requested from the contractor.
3. Dickinson Ave Project: Resolve conflict and upgrades as needed
4. GUC LNG Facility- Expansion
5. Staton Mill Road (Fred Smith Asphalt Plant): Installing Bollards and SCADA
6. Joe Stocks Road: 4" PE Gas Main Ext. (7800')
7. Enclave(BCH) LT Hardee Road: 2" PE Main Ext.
8. Diamond Dr. (Shooting Range): 2" PE Main Ext. and Service Install
9. Grover Gaming (Tupper Dr.) 2" PE Main and Service Installation

Projects In-Planning

1. W. 3rd Street, Ayden (ABC Store): 2" PE gas main extension (TBD)
2. LT Hardee Road (Arbor Hills Subdivision): 2" PE gas main extension (TBD)
3. ECU Legacy Hall: Upgrading existing gas service (July)
4. Eppes School: Installing 4" PE from Elms St. to Legacy Hall (July)
5. ECU Baseball Field: Service Upgrade (August)
6. Grady White: Installation 4" PE Service/HDD Hwy 264 (TBD)
7. Gas Valve Repair: E. 14th St. (Quails Ridge), Dickinson and Dansey, and Greenville Blvd. (Brown and Wood Dealership), Greenville Blvd. (Gate 2)
8. Camille Dr.: 2" PE Gas Main Ext. (TBD)
9. Memorial Dr. and W. 5th St. (NCDOT Project): Relocating 6" PE Main (TBD)
10. Boviet Solar: Main Ext. and Gas Service (August – September)

Future Projects


1. Old Creek Road (Nipro): Industrial Customer, service size TBD
2. Oxford Ridge: 2" PE Gas Main Ext.
3. W. 9th Street- Isolated Steel
4. Carolina Craft (Hwy 43 N): 2" PE Gas Main Ext.

Projects On-Hold

1. MacGregor Downs Rd. (GUC Electric Substation): 4" PE main installation, service is to supply gas to GUC generators.
2. Cypress Glen: Complete gas main and service installation
3. Sugg Parkway (Apple Park: Mr. Beast): 2" PE gas services
4. E 10th. Street and US 264: Mears Group, Inc completed HDD, GUC will schedule new 6" PE install to connect to existing 6" PE.
5. ECU Oglesby: Replacing PVC Service

JULY 2025

Pitt County UCC

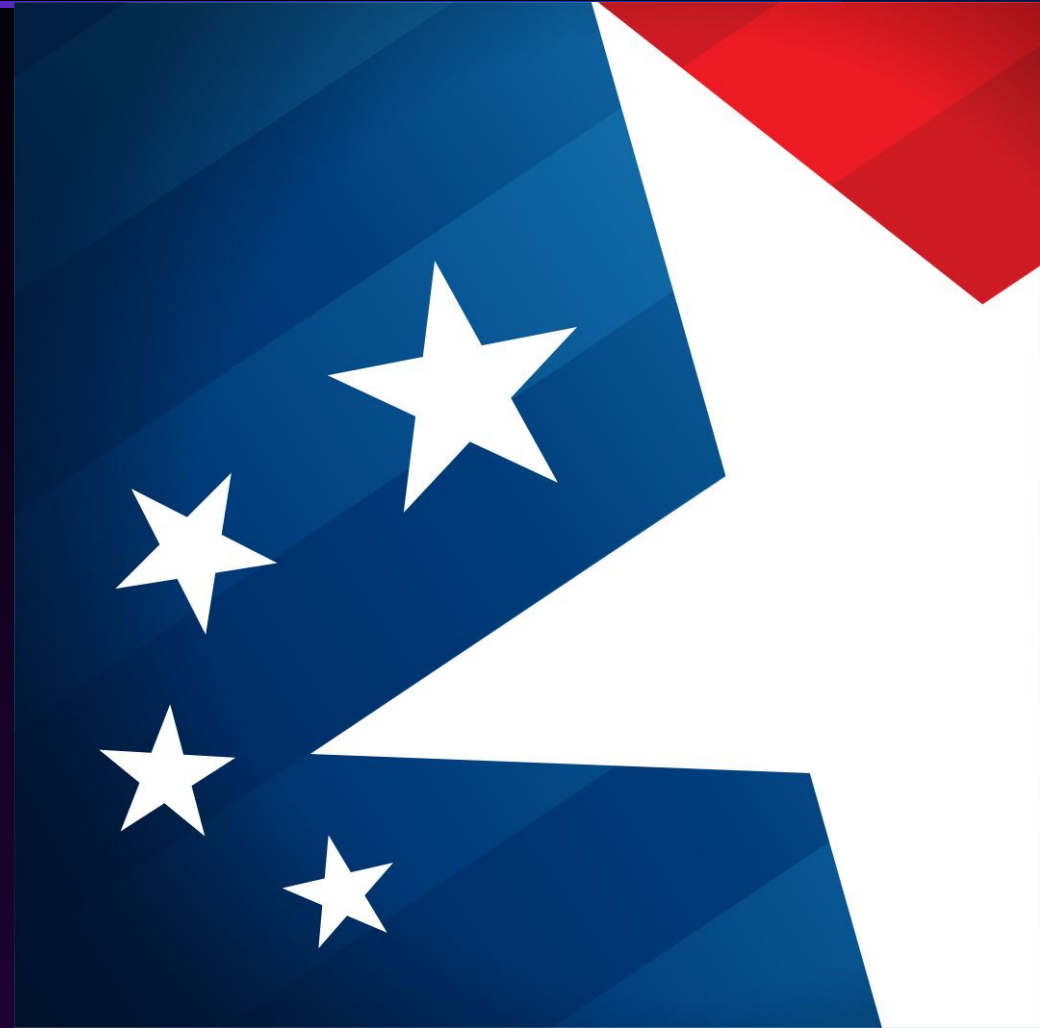



HOT WEATHER TIPS

- Alert workers to the heat index anticipated for the day and identify each precaution in place at the work site to reduce the risk of heat-related illness
- Provide plenty of cool drinking water and disposable cups
- Actively encourage workers to drink small amounts of water often
- Establish and enforce work/rest schedules
- Set up a buddy system
- Maintain effective communication with your crew at all times
- Encourage workers to wear sunscreen and use other protections from direct sunlight





MEETINGS

STATE UCC – July 8th, 10am
Charlotte Water, 5730 General Commerce Dr.

NCLRPC – July 16th, 11am
NC811 Greensboro Office

NC811 BOARD – July 18th, 8:30am
Crowne Plaza Resort, Asheville



STATE UCC SECRETARY NOMINATIONS

For a full listing visit


<https://ncucc.org/secretary-nominations/>





CALENDAR

NC811 & NCUCC EVENT
CALENDARS CAN BE
FOUND ON NC811.ORG
OR THE NC811 APP



DATA INSIGHTS


LOCATE REQUESTS

TRANSMISSIONS


COUNTY TICKET VOLUME

TOP 10 CALLERS

DAMAGE INFORMATION




LOCATE REQUESTS FOR NC JUNE 25 VS 24

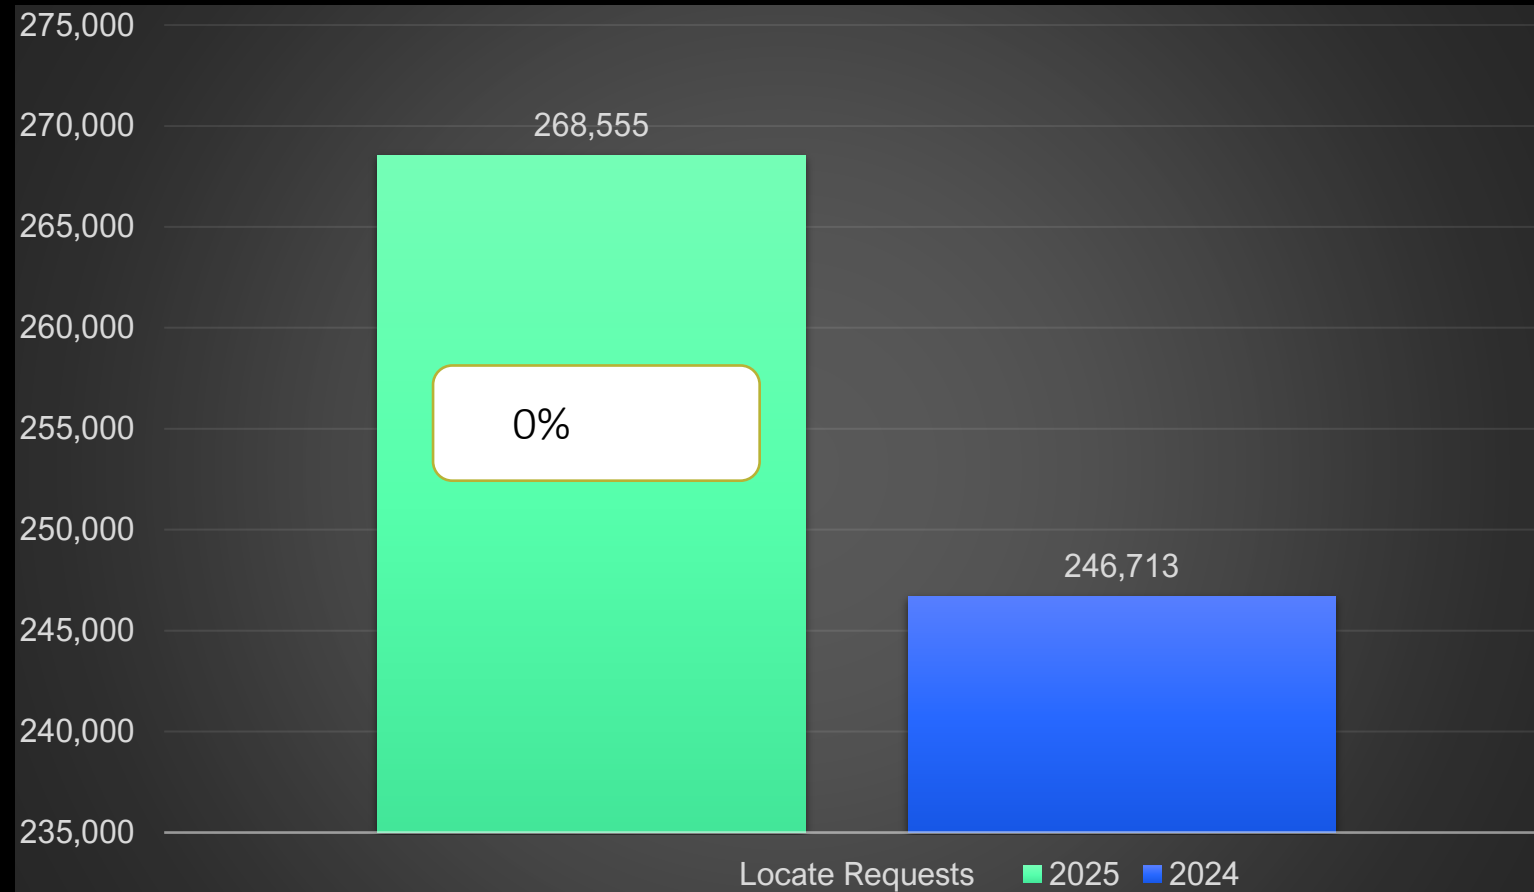


??

LOCATE REQUESTS FOR NC YEAR TO DATE

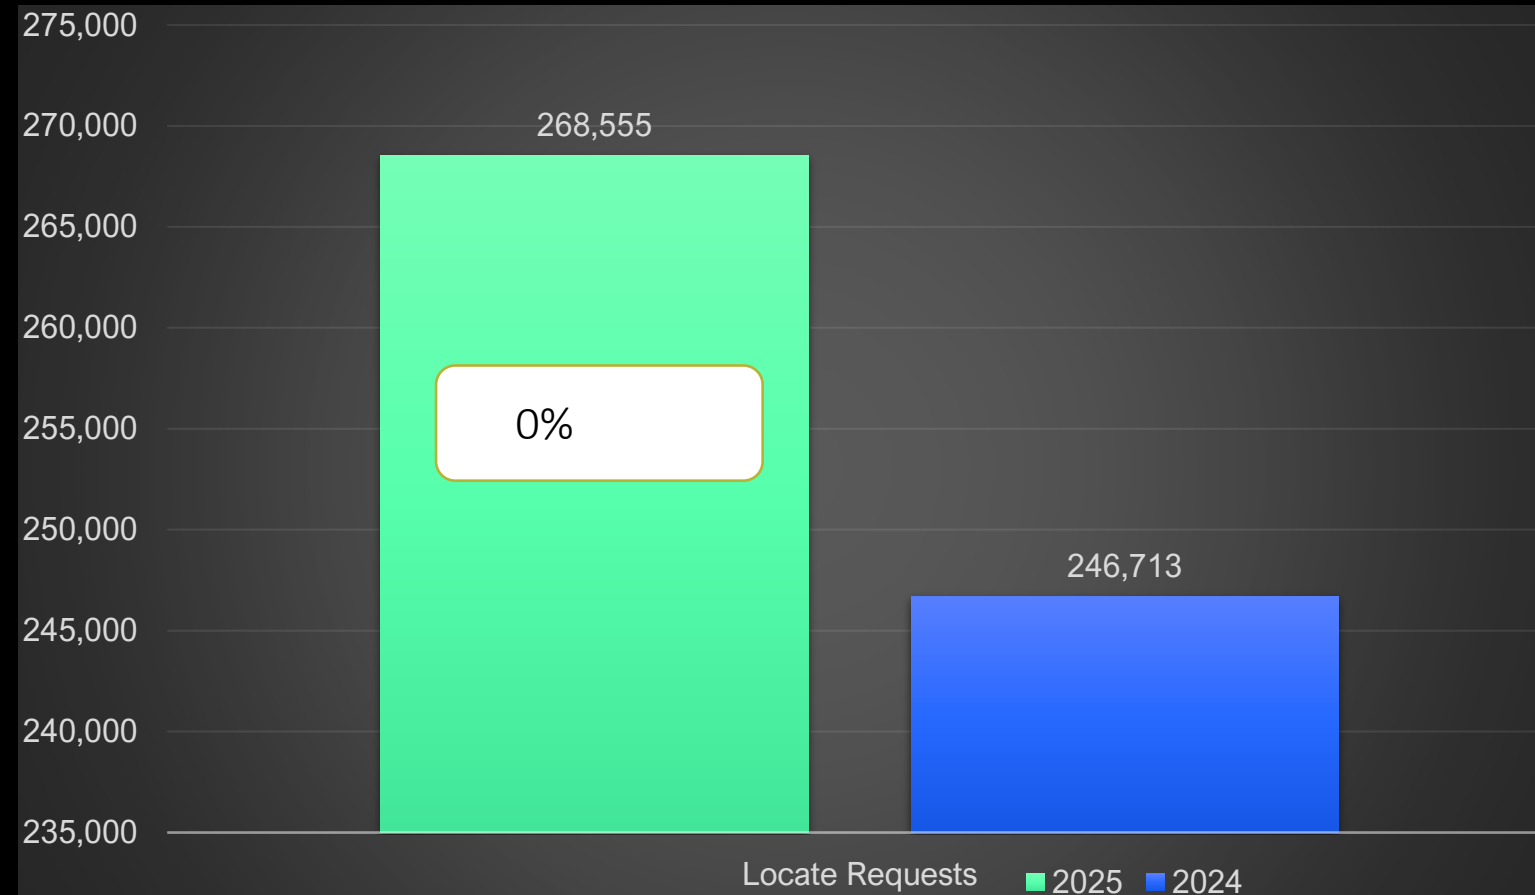


??

TRANSMISSIONS FOR NC JUNE 25 VS 24

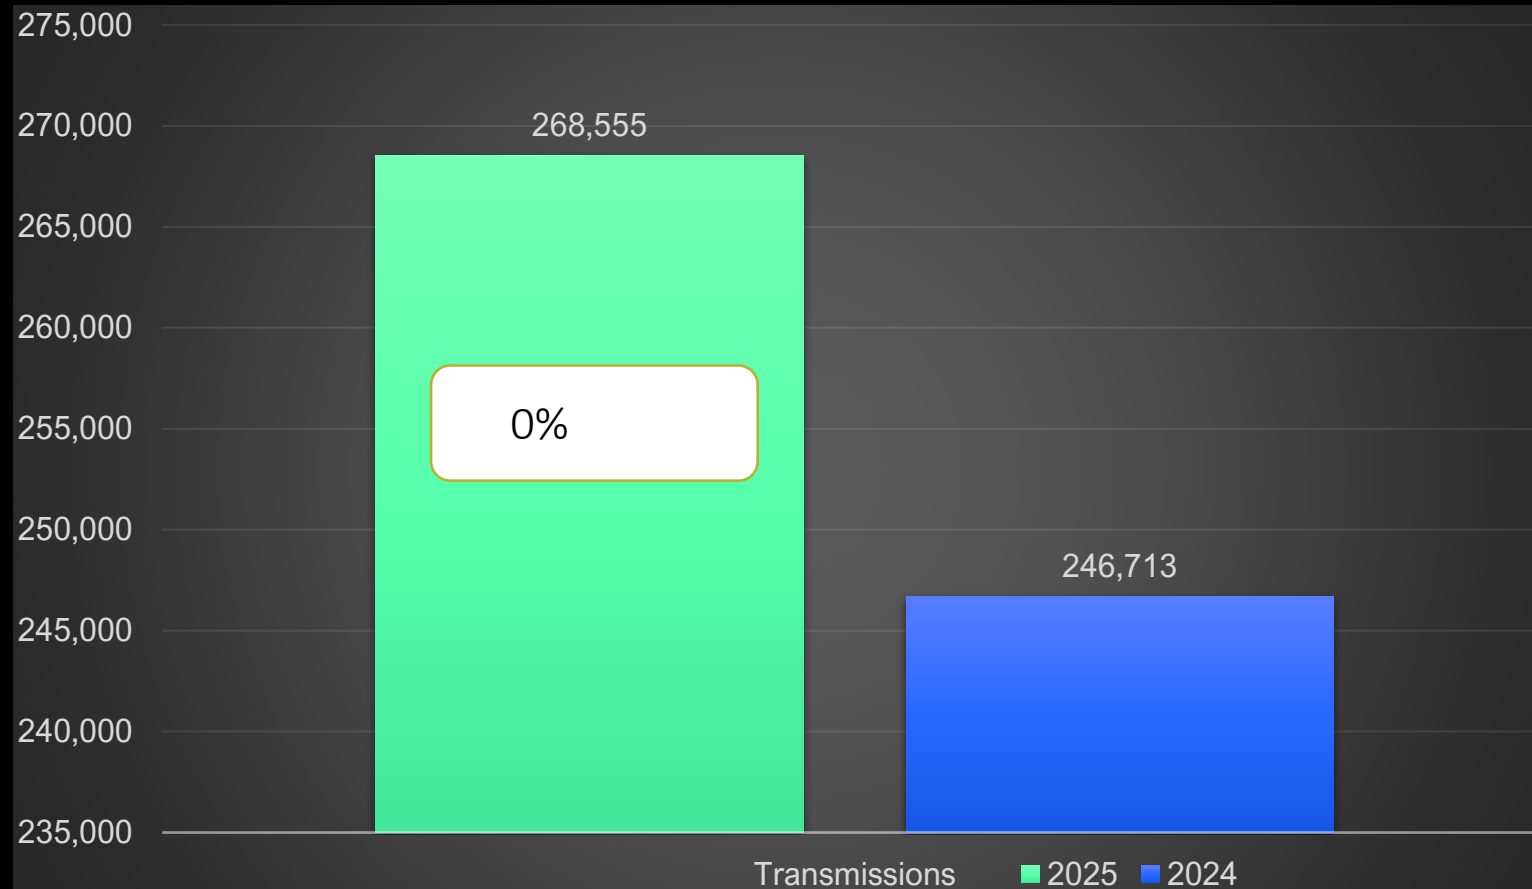

??

TRANSMISSIONS FOR NC JUNE 25 VS 24

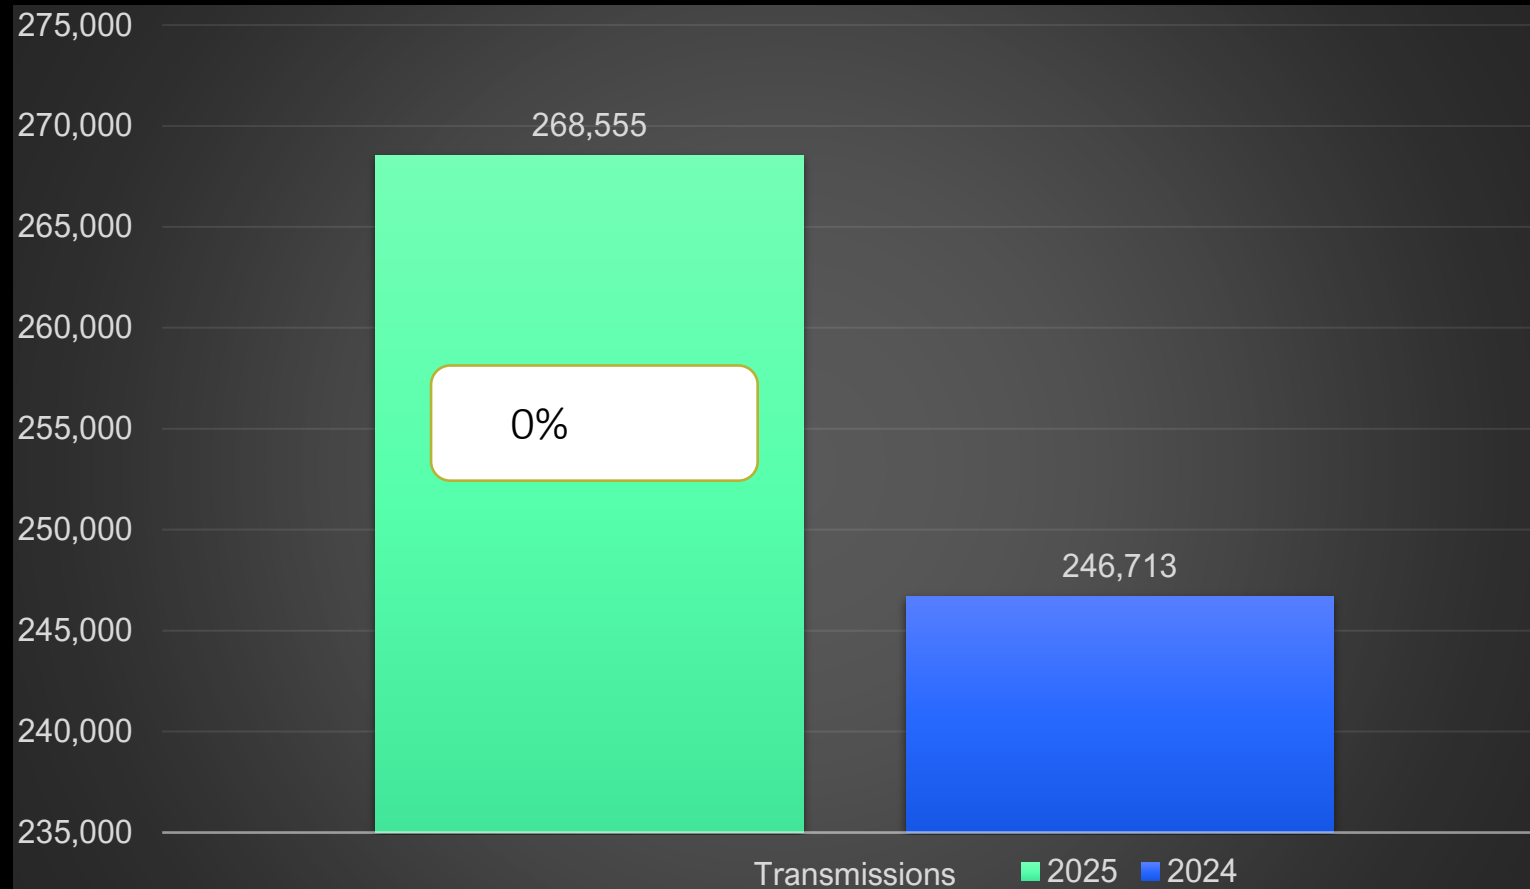

??



COUNTY TICKET VOLUME

JUNE 2025 VS 2024

Pitt	3 HR	CNCL	NEW	RXMT	UPDT	TOTAL Tickets
2024	100	21	1871	38	605	2635
2025	276	25	2383	36	824	3544
+/- Var	176.0%	19.0%	27.4%	-5.3%	36.2%	34.5%
		Avg Locates per Day				161



COUNTY TICKET VOLUME

YTD VS PREVIOUS YEAR

Pitt	3 HR	CNCL	NEW	RXMT	UPDT	TOTAL Tickets
2024	293	124	10196	174	3448	14235
2025	1720	198	14095	447	5125	21585
+/- Var	487.0%	59.7%	38.2%	156.9%	48.6%	51.6%
		Avg Locates per Day				170



COUNTY TICKET DISTRIBUTION

JUNE 2025

County/Place	06 Jun
PITT	3544
AYDEN	197
BEDFORD	1
BELL ARTHUR	2
BELL FORK	1
BELVOIR	7
BETHEL	25
BROOK VALLEY	1
CHICOD	21
CLAYROOT	2
DUPREE CROSSROADS	1
FALKLAND	7
FARMVILLE	103
FOUNTAIN	101
GREENBRIER	1

GREENVILLE	2285
GRIFTON	227
GRIMESLAND	150
LAKE ELLSWORTH	1
LYNNDAL	1
PACTOLUS	3
SIMPSON	6
STOKES	51
TUCKER ESTATES	1
WASHINGTON HEIGHTS	3
WHITEHURST	1
WINTERVILLE	345



TOP 10 CALLERS

JUNE 2025

Rank	Name	Totals
1	LAMBERTS CABLE SPLICING LLC	419
2	FUTURE COMMUNICATIONS	309
3	WILLIS CABLE CONSTRUCTION INC	241
4	GOLDMINE TECHNOLOGY SOLUTION CORP	197
5	BARNHILL CONTRACTING COMPANY	182
6	W G UNDERGROUND LLC	152
7	CAPE FEAR UTILITIES LLC	128
8	GREENVILLE UTILITIES COMMISSION	103
9	BAREFOOT COMMUNICATIONS INC	99
10	PALMETTO UNDERGROUND SOLUTIONS	94



DAMAGES

DIRT Damage Information
Reporting Tool

CGA Common
Ground
Alliance





DAMAGES BY COUNTY

JUNE 2025




DAMAGES PER 1,000 TRANSMISSIONS

JUNE 2025



Damages in North Carolina 2025 vs 2024

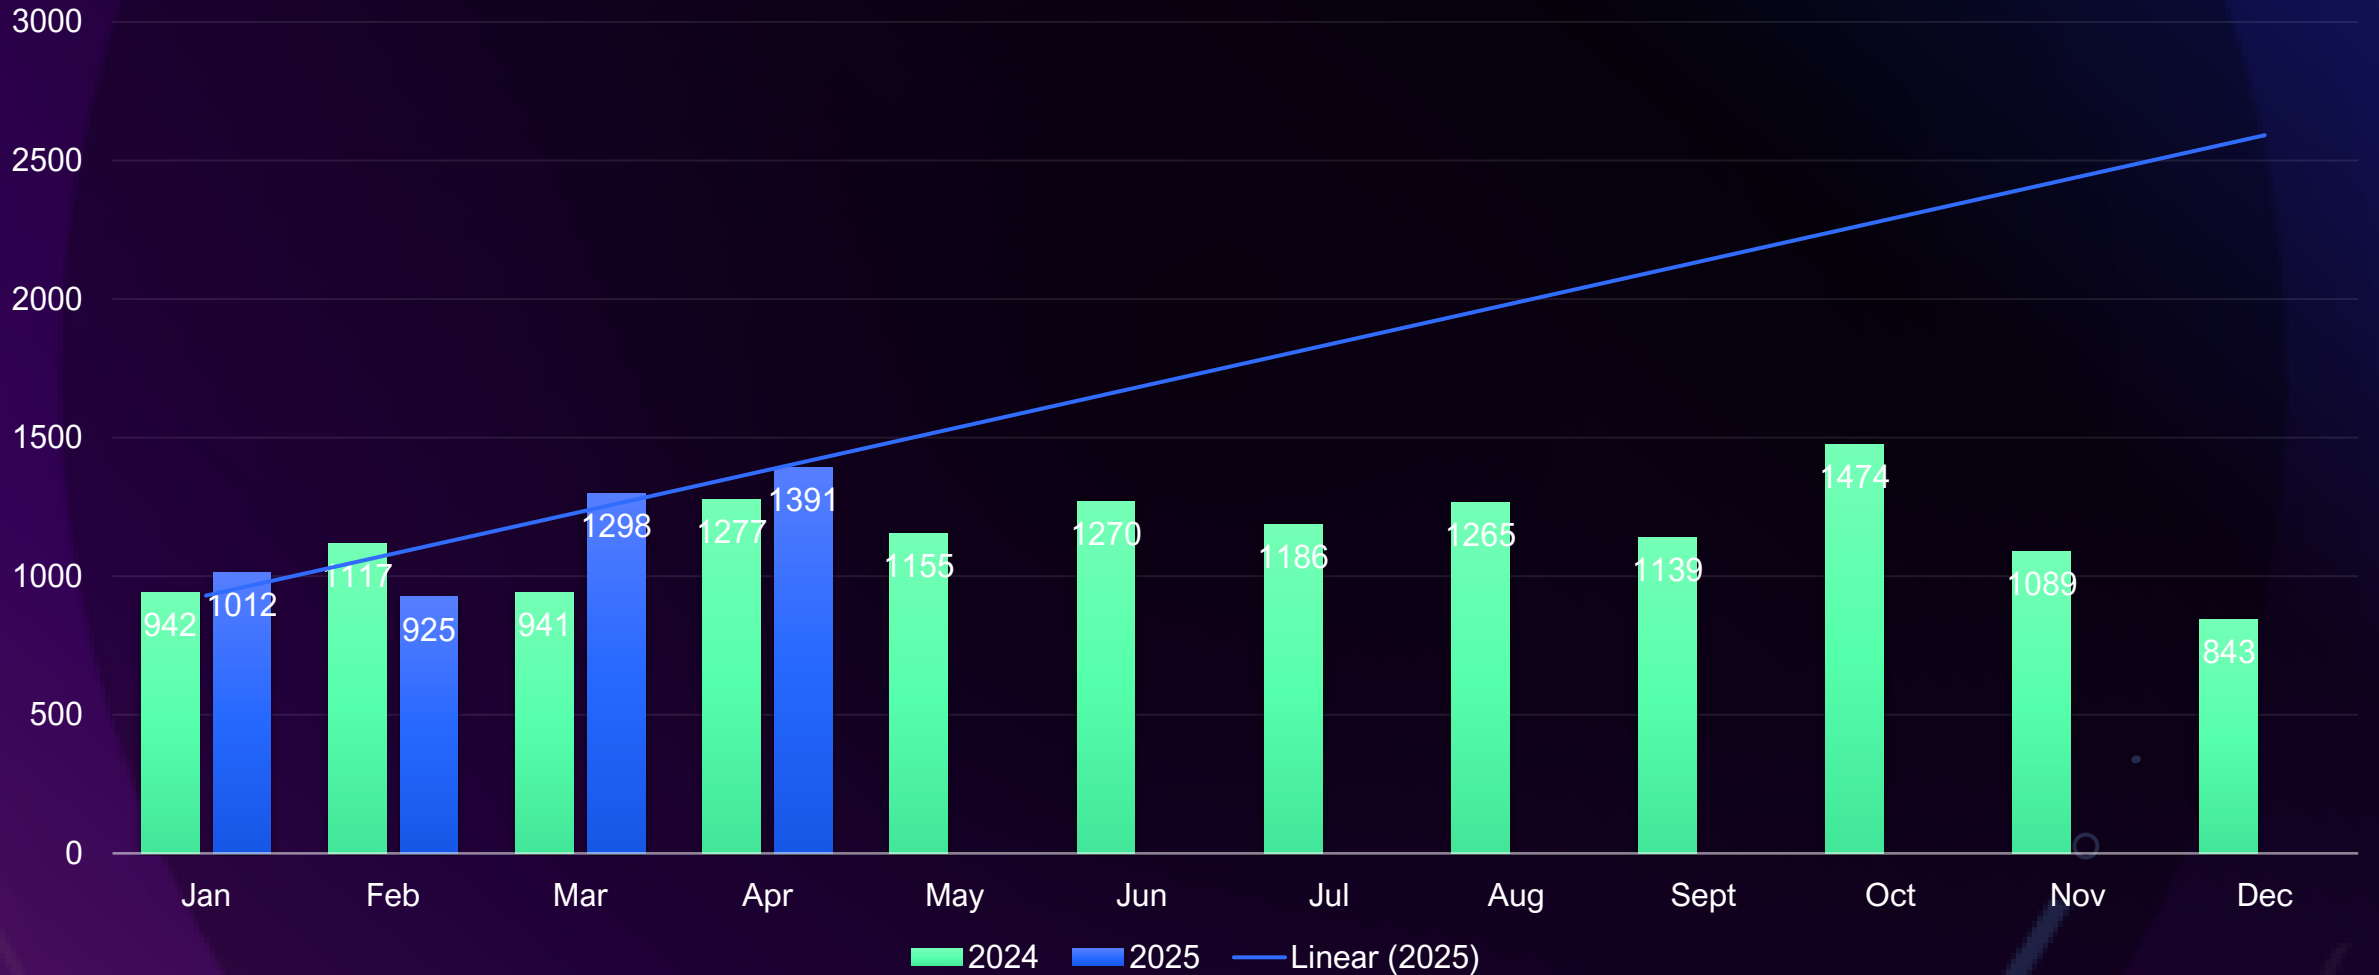

NC811 EDUCATION TEAM



Ann Rushing
Education Manager



Parrish Riddick
Education Liaison, Piedmont Region



Rory Phipps
Education Liaison, Western Region



Howard Corey
Education Liaison, Eastern Region



Tami Groves
Education Liaison, Southwest Region



Steve Moore
Media Relations Specialist

THANK YOU FOR YOUR ATTENTION



A copy of this presentation
will be available at
www.ncucc.org

